SOFTWARE PROJECT MANAGEMENT

SE-461

ACTIVITY-3

Project Title: Virtual Closet and Outfit Suggestion App

Instructor

Ms. Saima Imtiaz

Submitted By

Sajjal Khalil (4488-FOC/BSSE-F22-A)

Munazza Kanwal (4475-FOC/BSSE-F22-A)

Hajira Gul (4454-FOC/BSSE-F22-A)

Areesha Abbasi (4508-FOC/BSSE-F22-A)

Department of Software Engineering

International Islamic University, Islamabad

Perform the activity of dividing your projects next in breakdown structure and then assigning them number of day in the class duration and if you have made wbs then make network diagram.

1.Dividing the project into breakdown Structure:

Spaces

Virtual_Closet

Summary | Board | List | Calendar | Timeline | Approvals | Forms | Pages | Attachments | All work

Search list | Filter

Type	Key	Summary	Status	Comments	Due date
	VC-1	Requirements & Design	DONE	Add comment	Oct 22, 2025
	VC-20	Review and approve design specifications	DONE	Add comment	Oct 23, 2025
	VC-19	Design database schema for clothing metadata	DONE	Add comment	Oct 25, 2025
	VC-18	Create wireframes (mobile + web)	DONE	Add comment	Oct 29, 2025
	VC-17	Gather user requirements & use cases	DONE	Add comment	Nov 4, 2025
	VC-3	User Management & Auth	DONE	Add comment	Nov 7, 2025
	VC-23	Enable password reset and profile editing	DONE	Add comment	Nov 9, 2025
	VC-22	Implement authentication backend (JWT)	DONE	Add comment	Nov 10, 2025
	VC-21	Design signup/login screens	DONE	Add comment	Nov 11, 2025

Spaces

Virtual_Closet

Summary | Board | List | Calendar | Timeline | Approvals | Forms | Pages | Attachments | All work

Search list | Filter

Type	Key	Summary	Status	Comments	Due date
	VC-4	Virtual Wardrobe (Photo Upload & Catalog)	DONE	Add comment	Nov 12, 2025
	VC-27	Add image preview & validation	DONE	Add comment	Nov 13, 2025
	VC-26	Build tagging and categorization feature	DONE	Add comment	Nov 14, 2025
	VC-25	Implement storage system for images	DONE	Add comment	Nov 15, 2025
	VC-24	Develop image upload interface	DONE	Add comment	Nov 16, 2025
	VC-5	Outfit Suggestion Engine (AI)	IN PROGRESS	Add comment	Nov 17, 2025
	VC-28	Collect dataset of clothing images	IN PROGRESS	Add comment	Nov 17, 2025
	VC-29	Define rule-based outfit logic (weather, event, color)	IN PROGRESS	Add comment	Nov 17, 2025
	VC-30	Train and test AI model	IN PROGRESS	Add comment	Nov 17, 2025

Type	Key	Summary	Status	Comments	Due date
	VC-6	Weather & Occasion Integration	IN PROGRESS	Add comment	Nov 17, 2025
	VC-32	Add event/mood input functionality	IN PROGRESS	Add comment	Nov 17, 2025
	VC-31	Connect to weather API	IN PROGRESS	Add comment	Nov 17, 2025
	VC-7	UI / UX & Frontend App	TO DO	Add comment	Nov 30, 2025
	VC-34	Build closet view (grid layout)	TO DO	Add comment	Dec 3, 2025
	VC-33	Develop home screen and navigation	TO DO	Add comment	Dec 7, 2025
	VC-8	Testing & QA	TO DO	Add comment	Dec 9, 2025
	VC-36	Conduct integration tests	TO DO	Add comment	Dec 10, 2025
	VC-35	Write unit tests for backend modules	TO DO	Add comment	Dec 11, 2025

Type	Key	Summary	Status	Comments	Due date
	VC-36	Conduct integration tests	TO DO	Add comment	Dec 10, 2025
	VC-35	Write unit tests for backend modules	TO DO	Add comment	Dec 11, 2025
	VC-9	Deployment & Ops	TO DO	Add comment	Dec 12, 2025
	VC-38	Deploy on hosting platform	TO DO	Add comment	Dec 14, 2025
	VC-37	Set up CI/CD pipeline	TO DO	Add comment	Dec 15, 2025
	VC-10	Documentation & Handover	TO DO	Add comment	Dec 16, 2025
	VC-40	Write developer documentation	TO DO	Add comment	Dec 19, 2025
	VC-39	Create user manual and installation guide	TO DO	Add comment	Dec 20, 2025
	VC-11	Project Management & Review	TO DO	Add comment	Dec 22, 2025
	VC-43	Organize weekly review meetings	TO DO	Add comment	Dec 21, 2025
	VC-42	Conduct sprint planning	TO DO	Add comment	Dec 22, 2025
	VC-41	Conduct sprint planning	TO DO	Add comment	Dec 23, 2025

2. Network Diagram:

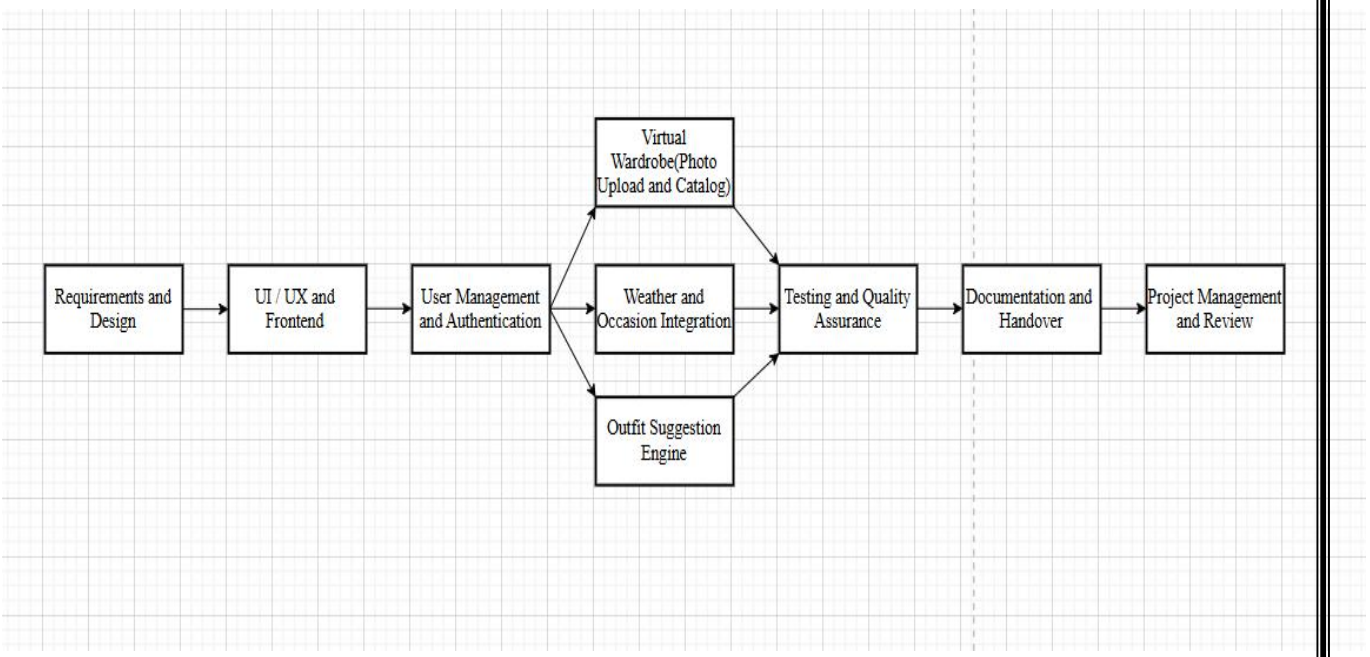

Reference:

https://virtualcloset123.atlassian.net/jira/core/projects/VC/list
